USF - Health Facilities Planning & Construction Project Status Update

Submitted by
Stan Douglas
HSC Facilities Director

Construction or Bid Phase Projects



USF – Health Facilities Planning and Construction

MDN 3rd Lab/Office Build-Out

Project Mgr: Stan Douglas/Maher Oueini



- Scope: Build-out ~ 2250
 SF 3rd unfinished space w/ labs, offices, PT rooms, & lobby
- Status: Bid Phase (Bid Opening date 10-15-08)
- Budget: ~\$375,000
- Funding Source: Nursing Dept Funding

Picture of Current 3rd Floor Unfinished Space


USF – Health Facilities Planning and Construction MDC 4007 Renovation/Reconfiguration – PM Stan Douglas



- Scope: Renovation and reconfigure 635 SF lab/office suite
- Status: Construction (estimated completion mid-Oct 08)
- Budget: \$40,000Contract Amt: \$65,000
- Funding Source: PECO 06-07 & 07-08

MDC 4007 Before Construction Start

USF – Health Facilities Planning and Construction MDL Microscopy/Imaging Laboratory Project Manager: Stan Douglas

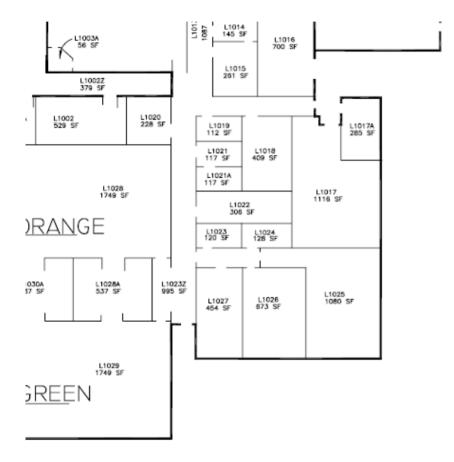


MDL Microscopy Space Layout

- Scope: Renovate and Upgrade interior surface finishes in MDL spaces in support Microscopy function. These spaces include the entrance/passage way to and thru the area, along with refurbishing rooms, L1023, L1025, L1024, L1022, & L1018, L1020, L1015, L1014. Area L1017 will be converted to a Histology Lab
- Status: Construction 90% Complete
- Budget: \$1,200,000
- Funding Source: PECO & Private Donor

USF – Health Facilities Planning and Construction

MDL Microscopy/Imaging Laboratory Project Manager: Stan Douglas

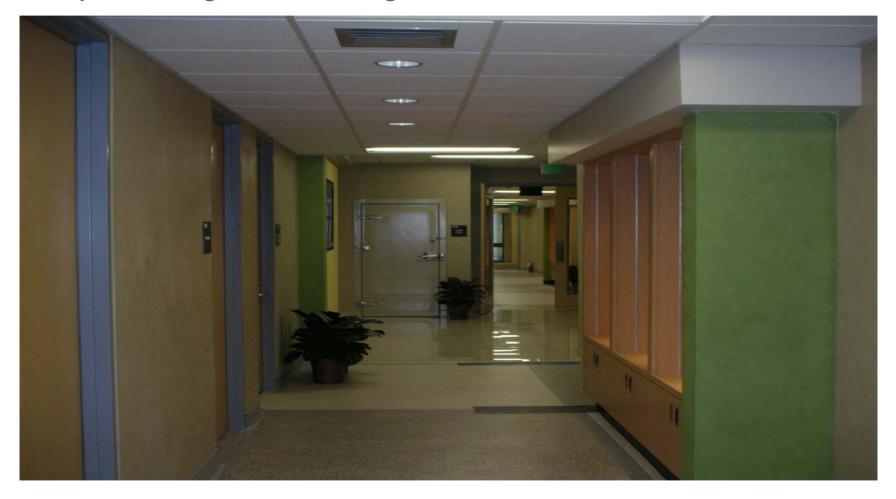


USF – Health Facilities Planning and Construction Other Project Scheduled for October 2008 Completion

 USF HEALTH (IT) Notification Monitors (Budget -\$87,000)
 Funding Source – PECO 07-08

 COPH Install Additional Security Camera (Budget \$10,000) Funding Source PECO 07-08

Design & Development Phase Projects

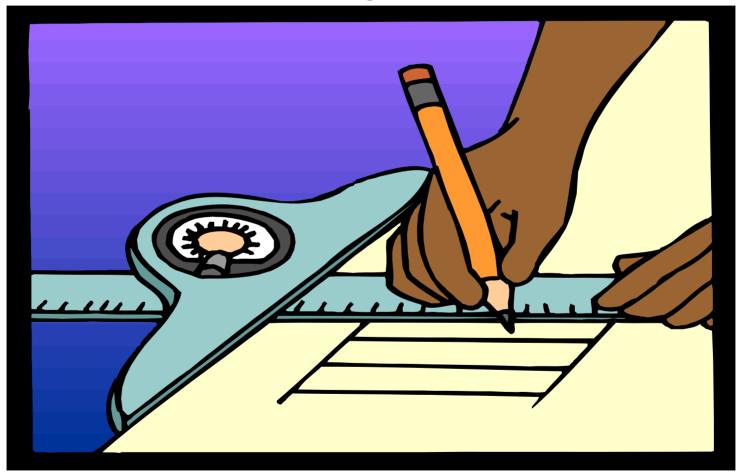

USF – Health Facilities Planning and Construction

Update and Reconfigure HSC Fire Alarm System Project Mgrs: Stan Douglas & Maher Oueini



- Scope: Project involves a redesign and updating the current antiquated fire alarm system for MDC, MDL, MDA, & MDE.
 Design package will be developed w/ phased construction delivery.
- Status: Design Complete (Construction will be executed in phases)
- Budget: \$71,000
- Funding Source: PECO 07-08

Picture of Main HSC Fire Alarm Panel

USF – Health Facilities Planning and Construction

V. A. Pedestrian Walkway Facility Repairs

Project Manager: Stan Douglas



View of Skyway Underside

- Scope: Work involves concrete restoration, crack repair, strengthening of existing walkway structure
- Status: Design 95% complete
- Budget: Design Fees currently \$54K.
 Construction cost estimate ~ \$300K (VA to share cost)
- Funding Source: Capital Renewal/PECO 07-08

USF – Health Facilities Planning and Construction MDC Replace Vivarium Boilers – PM Oscar Figueroa/Stan


Douglas



- Scope: Replace 2-40 hp boilers for cage wash down area
- Status: Design Phase
- Budget: \$100,000
- Cost Estimate: \$150,000
- Funding Source: PECO 07-08

Picture of existing boilers

Programming/Planning Phase Projects

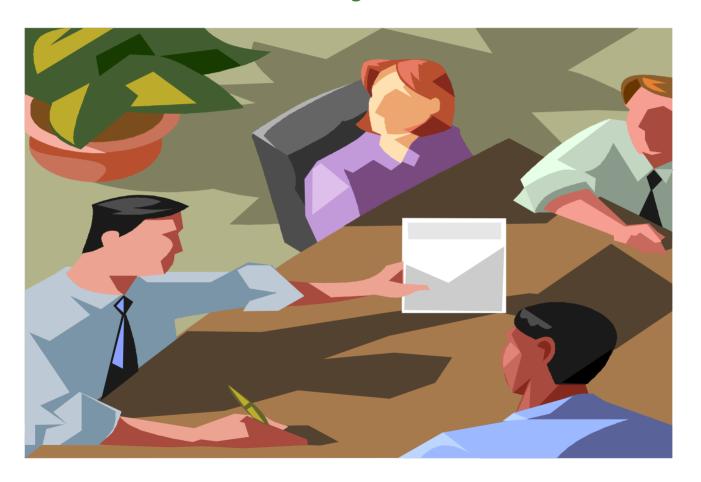

USF – Health Facilities Planning and Construction MDL Upgrade Anatomy Lab Project Mgr: Stan Douglas



- Scope:
 Refurbish/renovation/
 upgrade existing
 lab/office/prep spaces to
 support academic vision
 of the medical school
- Status: Planning/Programming (Customer's Program Documents Pending)
- Budget: \$60,000
- Funding Source: PECO 07-08

Picture of Current Anatomy Lab

USF – Health Facilities Planning and Construction MDC Expand USF HEALTH IT Server Room Project Mgr: Stan Douglas/Maher Oueini



- Scope: Reconfigure and increase the size of the current IT Server room to accommodate HEALTH IT expansion.
- Status: Programming
- Budget: TBD

Funding Source: TBD

Picture of existing Network Ops Center

USF – Health Facilities Planning and Construction Other Key Projects in Programming/Development Phase

- MDL Install Hyperbaric Lab Tank Farm & Lab Modifications (Cost Estimate in Development) Funding Source – Dept/PECO
- MDA 1200 Renovate USF HEALTH Auditorium Cost Estimate \$122,601 Funding Source PECO 07-08
- COPH Replace Cage Washer (Cost Estimate TBD)
 Funding Source Dept
- MDC Evaluate HR Space for Educational Affairs (Cost Estimate TBD)
 Funding Source TBD
- MDC 3045, 3026, & 3030 Research Lab Renovations Cost Estimate \$40,000 Funding Source PECO 07-08

Recently & Earlier Completed Renovation Projects



USF – Health Facilities Planning and Construction MDT Lecture/Classroom 1100 Project Mgr – Maher Oueini



- Scope: Renovate/upgrade lecture space w/ new finishes and electronics package
- Status: Construction complete
- Budget: \$87,000
- Actual Cost: \$66,578.00
- Funding Source: PECO 07-08

MDT Classroom 1100 newly renovated

USF – Health Facilities Planning and Construction MDC Renovate Lab/office spaces 2029-2036 Project Mgr: Stan Douglas



- Scope: Reconfigure ~ 1100 SF of existing office/lab suite for Pathology Dept
- Status: Construction Complete
- Budget: \$200,000
- Actual Cost: ~ \$230,000
- Funding Source: PECO 07-08

Picture of renovated lab Space

USF – Health Facilities Planning and Construction MDC Renovate Various Lab/office spaces Project Mgr: Stan Douglas





Renovated MDC 3012/3015 Lab

- Scope:
 Renovate/Refurbish lab
 and study areas MDC
 3012 & 3015, respectively
 for Molecular Medicine
 Dept.
- Status: Construction complete
- Budget: \$100,000
- Actual Cost: \$115,755
- Funding Source: PECO 07-08

USF – Health Facilities Planning and Construction List of Other Completed Projects and Final Cost

- MDC Refurbish AHU #6 \$41,682 (Budget \$50,000) PECO 07-08
- MDC 3111 Flow Lab Renovation \$47,127 (Budget \$80,000)
 PECO 06-07
- MDC Lab 4028 Renovation \$14,694 (n/a) PECO 06-07
- MDL 1005 Classroom/Lecture Room Renovation -\$310,561(Budget \$320,000) PECO 06-07
- COPH Lab Renovations \$247,000 PECO 05-06
- MDC 1031 Business Office Renovation \$55,898 (Budget \$50,000) Dept Funding
- HSC Infra-Structure Repair VA Skyway Roof Ridge Cap \$47,369
 12/9/2(Budget \$50,000) PECO 06-07

If your department's project is not shown or listed in this report...the details of the project scope are in development and will be included in the next update.

Thanks ©
